


APPENDIX B

# 2024 4th Quarter Review

## Infrastructure

Monty Doonanco – Manager of Transportation

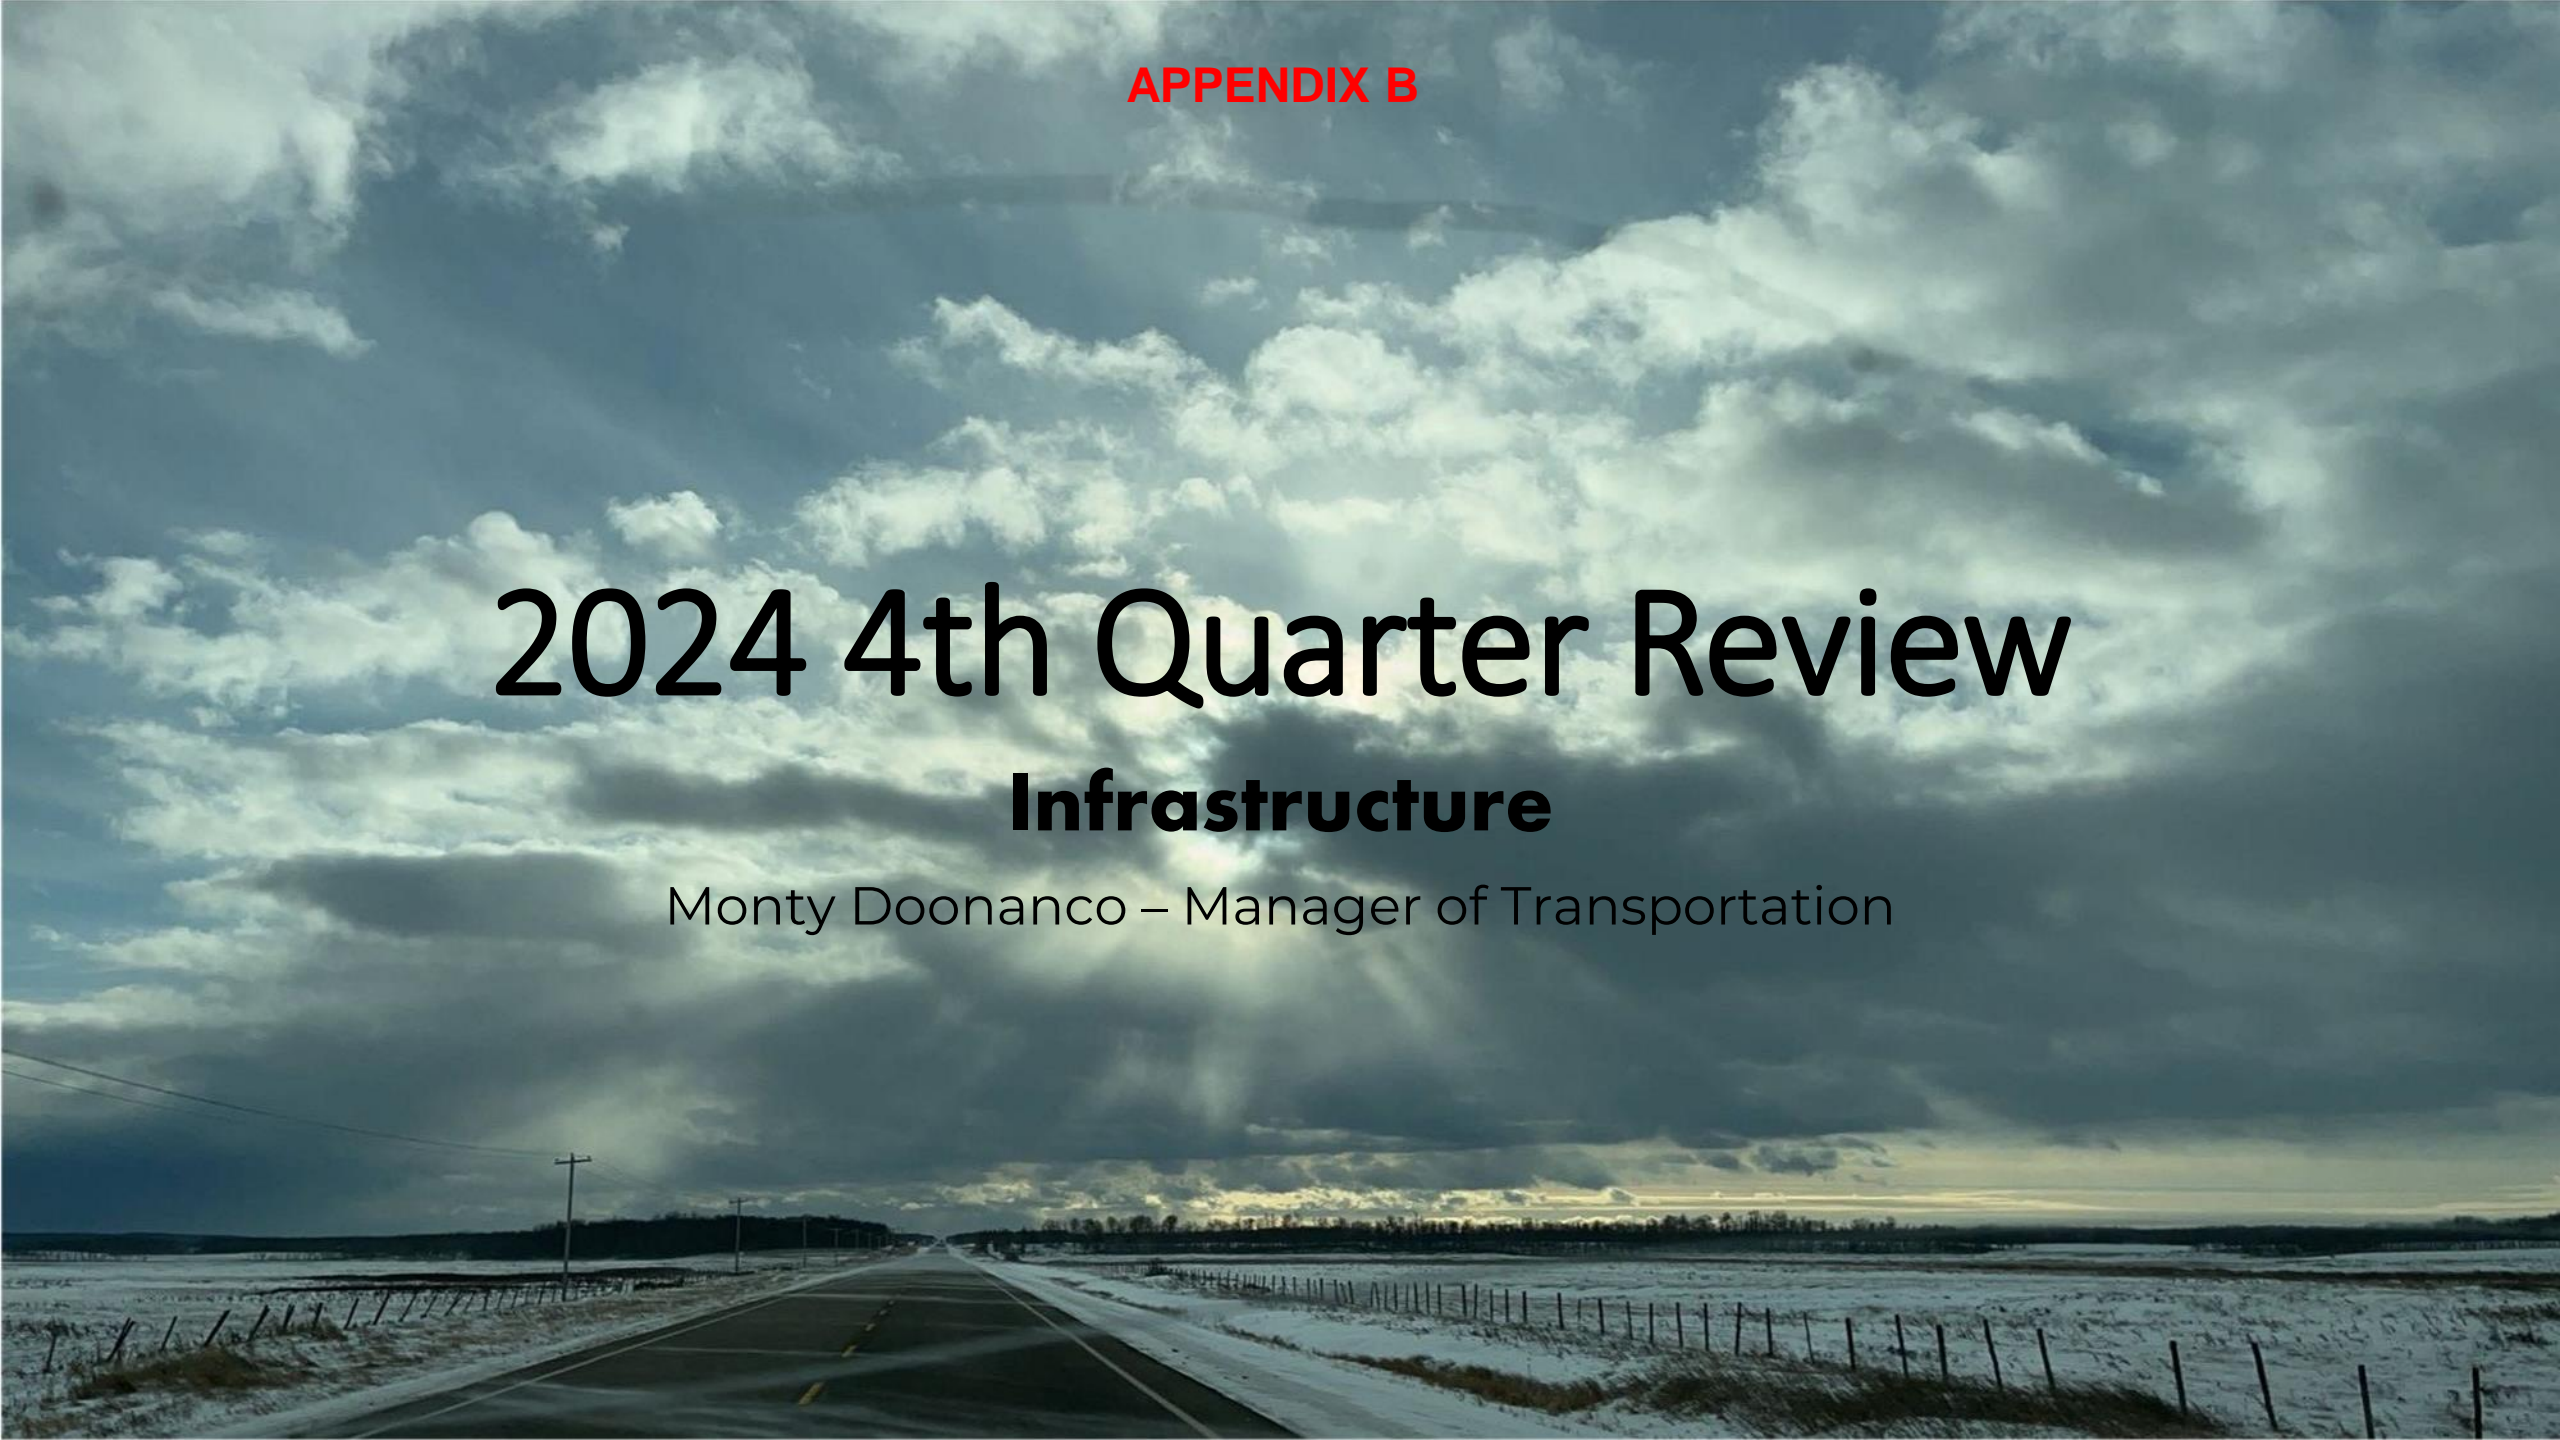



# 2024 Design Build of Cherry Grove Firehall & Grader Shop

- Pile foundation has been completed.
- Utility providers have installed gas and power services.
- Buried cisterns and septic tank have been installed.
- Prefab building frame was delivered from supplier and has been erected.
- Wall panel installation is underway.





## 2024 Installation of Backup Generators

- Concrete pads and all conduits have been placed for both the Main Administration Building and the Kinosoo Chalet installation locations.
- Delivery of generators were delayed. As a result, the generators will be installed in the spring.





# Reconstruction

TWP 622 from RR  
470 to RR 474

- This project includes grading, gravel base and paving work. It was re-tendered in November and a contractor was awarded the work. This project is anticipated to be completed in Q2/Q3.





# Culverts & Bridges

## **BF72515 (Truman Bridge: RR 485, North of TWP 630)**

- Detailed inspection and engineering assessment was performed after collision. Repair/replacement options to be reviewed with Council.

## **BF72208 (TWP 630, West of RR 471)**

- Department of Fisheries & Oceans approval of the design was received on Sept 26, which did not allow enough time to complete the work in 2024. Ordered materials were received at the MD yard on Nov 3 for winter storage and contractor is planning to install this year.

## **BF71791 (RR 480, South of TWP 610)**

- Culvert replacement was completed by our contractor at the end of October.





## Purchase: Calcium Sand

- 2000 tonnes of calcium sand was purchased and hauled into the Public Works yard and is to be used in winter sanding operations.



## Purchase: Survey Equipment

- Our new survey gear replaces outdated equipment. It features improved and additional functions and is very user friendly.





Questions, comments, concerns?
